


5/8 TO 5/12
COMPLETED

5/15 TO 5/19

5/22 TO 5/26

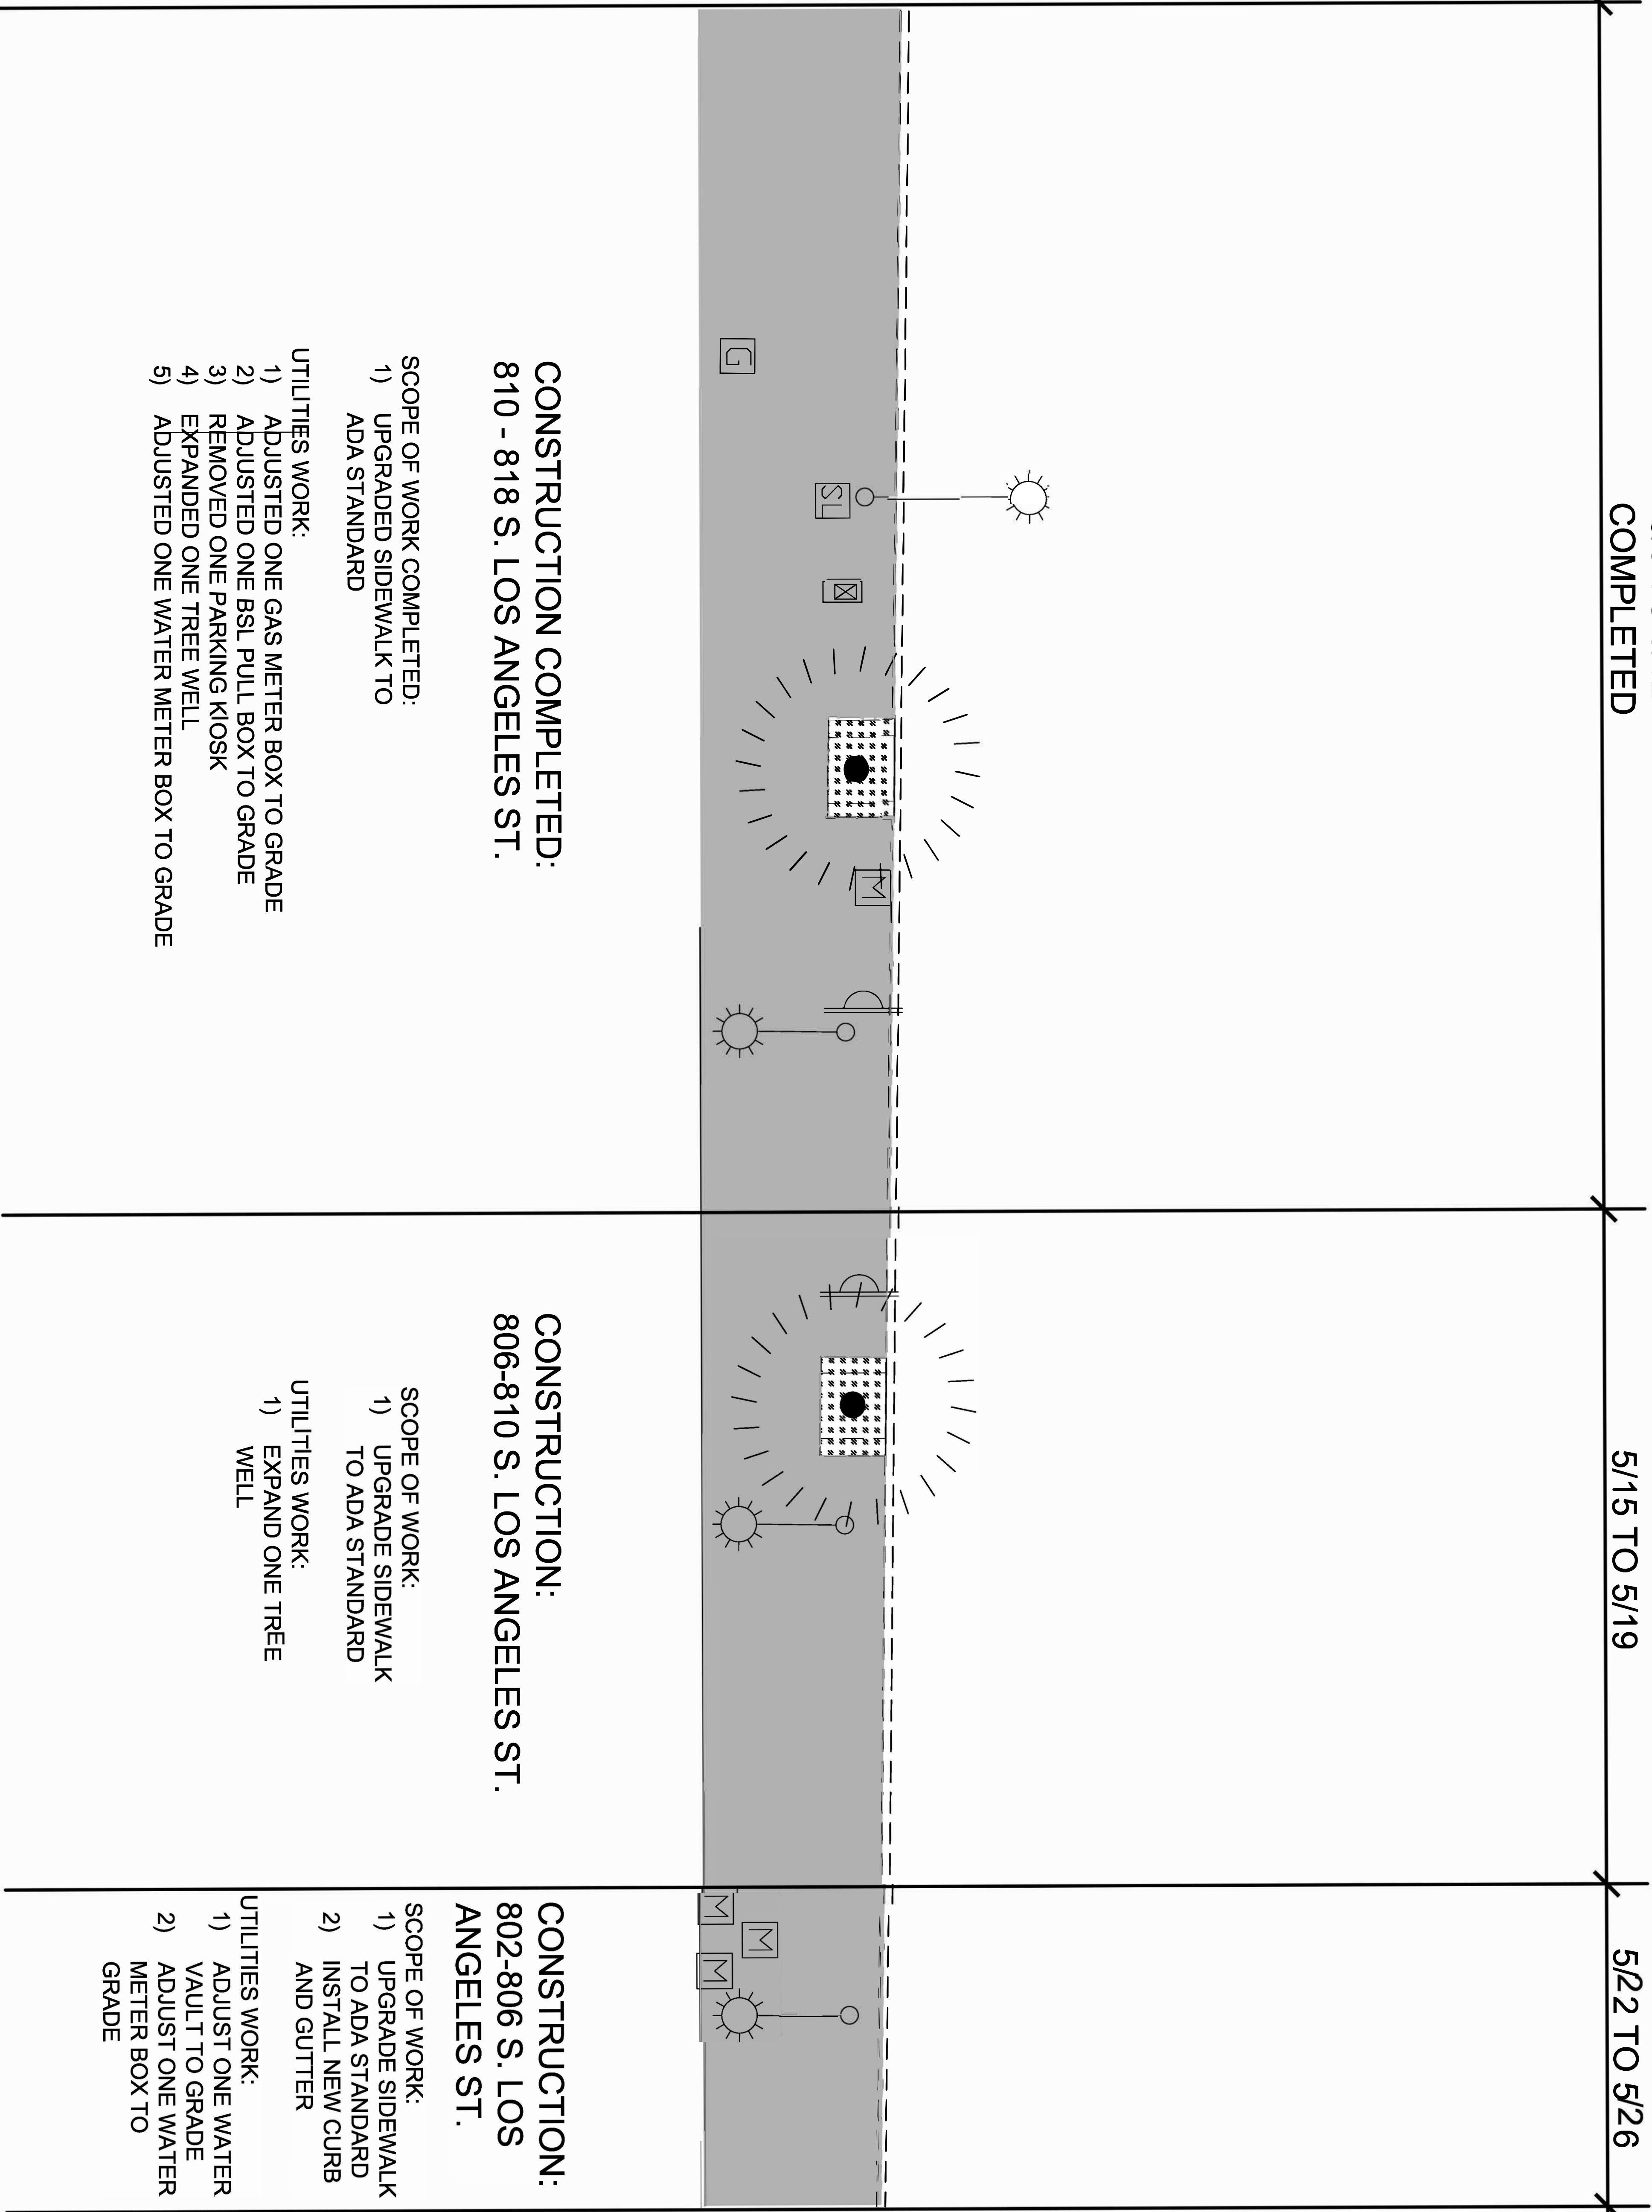

CONSTRUCTION COMPLETED:
810 - 818 S. LOS ANGELES ST.

SCOPE OF WORK COMPLETED:
1) UPGRADED SIDEWALK TO ADA STANDARD

- UTILITIES WORK:**
- 1) ADJUSTED ONE GAS METER BOX TO GRADE
 - 2) ADJUSTED ONE BSL PULL BOX TO GRADE
 - 3) REMOVED ONE PARKING KIOSK
 - 4) EXPANDED ONE TREE WELL
 - 5) ADJUSTED ONE WATER METER BOX TO GRADE

CONSTRUCTION:
806-810 S. LOS ANGELES ST.

SCOPE OF WORK:
1) UPGRADE SIDEWALK TO ADA STANDARD

- UTILITIES WORK:**
- 1) EXPAND ONE TREE WELL


CONSTRUCTION:
802-806 S. LOS ANGELES ST.

SCOPE OF WORK:
1) UPGRADE SIDEWALK TO ADA STANDARD
2) INSTALL NEW CURB AND GUTTER


- UTILITIES WORK:**
- 1) ADJUST ONE WATER VAULT TO GRADE
 - 2) ADJUST ONE WATER METER BOX TO GRADE

2-WEEK CONSTRUCTION SCHEDULE

N.T.S.



SCALE: NOT TO SCALE

CITY OF LOS ANGELES		DEPARTMENT OF PUBLIC WORKS		BUREAU OF STREET SERVICES																	
WORK ORDER NO. M0014217 DRAWING NO. C-16	SHEET TITLE : FASHION DISTRICT PHASE II CONSTRUCTION SCHEDULE - 5/15 TO 5/26 PROJECT : FASHION DISTRICT PHASE II STREETSCAPE PROJECT ADDRESS: S.LOS ANGELES ST BETWEEN OLYMPIC BLVD AND 7TH ST.	PRINCIPAL CIVIL ENGINEER DATE: _____ HUGH S. LEE, S.E., C.C.S.	NAZARIO SAUCEDA DIRECTOR ENGINEERING DIVISION INITIAL DATE DESIGNED BY :LAWRENCE LIN CHECKED BY: NAME APPROVED BY: NAME PROJECT MGR: NAME	<table border="1" style="width: 100%; border-collapse: collapse;"> <thead> <tr> <th>NO.</th> <th>REVISION DESCRIPTION</th> <th>DATE</th> <th>BY</th> </tr> </thead> <tbody> <tr><td> </td><td> </td><td> </td><td> </td></tr> <tr><td> </td><td> </td><td> </td><td> </td></tr> <tr><td> </td><td> </td><td> </td><td> </td></tr> </tbody> </table> WORK ACCEPTED SERIAL NO. INDEX NO.	NO.	REVISION DESCRIPTION	DATE	BY													 BUREAU OF STREET SERVICES DEPARTMENT OF PUBLIC WORKS CITY OF LOS ANGELES
NO.	REVISION DESCRIPTION	DATE	BY																		
